


11/14/25 1ST AVE-DISTRICT 8 CONSTRUCTION SCHEDULE

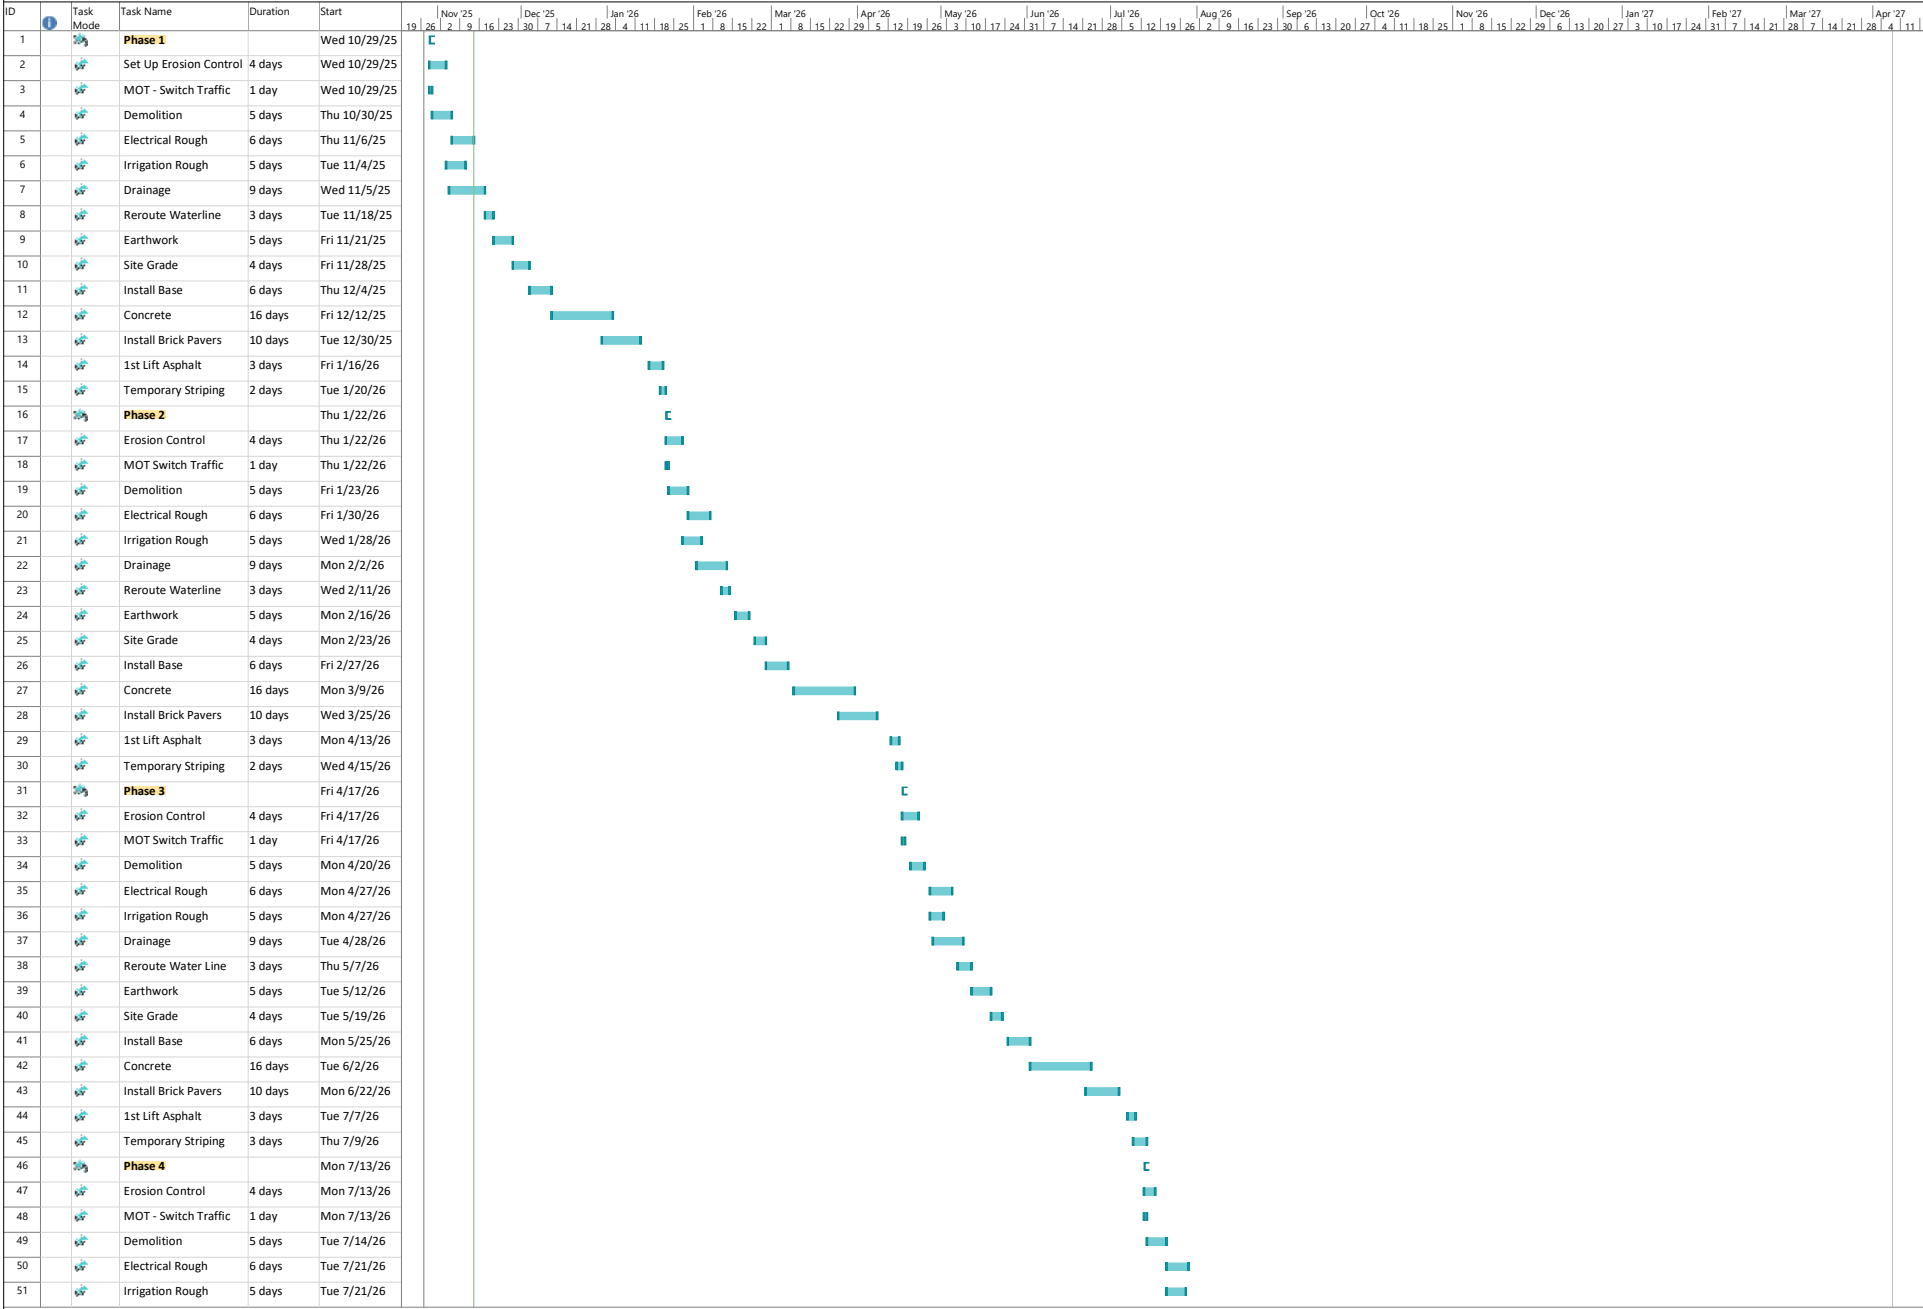

Project: Foster Road Schedule
Date: Fri 11/14/25

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	

11/14/25 1ST AVE-DISTRICT 8 CONSTRUCTION SCHEDULE

ID	Task Mode	Task Name	Duration	Start
52	🚧	Drainage	9 days	Wed 7/22/26
53	🚧	Reroute Waterline	3 days?	Fri 7/31/26
54	🚧	Earthwork	5 days	Wed 8/5/26
55	🚧	Site Grade	4 days?	Wed 8/12/26
56	🚧	Install Base	6 days	Tue 8/18/26
57	🚧	Concrete	16 days	Wed 8/26/26
58	🚧	Install Brick Pavers	10 days	Tue 9/15/26
59	🚧	1st Lift Asphalt	3 days?	Wed 9/30/26
60	🚧	Temporary Striping	2 days	Fri 10/2/26
61	🚧	Phase 5		Tue 10/6/26
62	🚧	Erosion Control	4 days	Tue 10/6/26
63	🚧	MOT - Switch Traffic	1 day	Tue 10/6/26
64	🚧	Demolition	5 days	Wed 10/7/26
65	🚧	Electrical Rough	6 days	Wed 10/14/26
66	🚧	Irrigation Rough	5 days	Wed 10/14/26
67	🚧	Drainage	9 days	Thu 10/15/26
68	🚧	Reroute Waterline	3 days?	Mon 10/26/26
69	🚧	Earthwork	5 days	Thu 10/29/26
70	🚧	Site Grade	4 days?	Thu 11/5/26
71	🚧	Install Base	6 days	Wed 11/11/26
72	🚧	Concrete	16 days	Thu 11/19/26
73	🚧	Install Brick Pavers	10 days	Wed 12/9/26
74	🚧	1st Lift Asphalt	3 days?	Thu 12/24/26
75	🚧	Temporary Striping	2 days	Mon 12/28/26
76	🚧	Phase 6		Wed 12/30/26
77	🚧	Erosion Control	4 days	Wed 12/30/26
78	🚧	MOT - Switch Traffic	1 day	Wed 12/30/26
79	🚧	Demolition	5 days	Thu 12/31/26
80	🚧	Electrical Rough	6 days	Thu 1/7/27
81	🚧	Irrigation Rough	5 days	Thu 1/7/27
82	🚧	Drainage	9 days	Fri 1/8/27
83	🚧	Reroute Waterline	3 days?	Tue 1/19/27
84	🚧	Earthwork	5 days	Fri 1/22/27
85	🚧	Site Grade	4 days?	Fri 1/29/27
86	🚧	Install Base	6 days	Thu 2/4/27
87	🚧	Concrete	16 days	Fri 2/12/27
88	🚧	Install Brick Pavers	10 days	Thu 3/4/27
89	🚧	1st Lift Asphalt	3 days?	Fri 3/19/27
90	🚧	Temporary Striping	2 days	Tue 3/23/27
91	🚧	Irrigation Heads and Landscape	25 days	Fri 1/8/27
92	🚧	Decorative Columns	26 days	Thu 2/4/27
93	🚧	Streetlight Festoon Lighting/Pole/Fixture Installion	30 days	Tue 2/23/27
94	🚧	Final Lift of Asphalt	4 days	Wed 3/17/27
95	🚧	Final Striping Striping	3 days	Tue 3/23/27
96	🚧	Punch Out	5 days	Fri 3/26/27
97	🚧	Final Thermoplastic Pavement Marking	4 days	Fri 4/2/27

Project: Foster Road Schedule
Date: Fri 11/14/25

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	
